

Group Research Project - Assignment 1

Group Members:

Dhruv Patel (Leader): Student ID: 21564183

Rutvi Rakholia: Student ID: 21560827

Moin Madhani: Student ID: 21564182

Akarshit Mahajan: Student ID: 21555043

Table of contents

Introduction

Literature Review

- Team Charter
- Project Charter

Project Planning

- Gantt Chart
- Work Breakdown Structure
- Sprint Backlog
- Risk Analysis

Requirement Analysis

- Company Background
- Project Scope
- User Stories
- User Journey

Evidence of Website/Online Store

- Layouts
- Screenshots
- Plugins

Website Go through and Testing

Reference

Link to the website: <https://sugarsprout.store/>

Introduction

This document serves as the culmination of our Group Research Project outlining our approach, methodology, and the key features incorporated into our e-Commerce website in response to a hypothetical scenario presented by a retail company. This document also reflects our team efforts, innovative ideas, and dedication in delivering this project.

Literature Review

This literature review emphasizes the suitability of Agile methodology for our e-Commerce website development project. We have discussed the importance of project management, teamwork, and the tools/software utilized. Additionally, it provides a structured Work Breakdown Structure (WBS) with task categories for effective project planning and execution within the Agile framework.

1. **Advantages and disadvantages of Waterfall and Agile method:** Development methodologies refer to the systematic approaches used to structure, plan, and control software development projects. Two primary methodologies are the Waterfall and Agile methods. Starting with WaterFall Method, it is a linear software development approach where each phase, including Requirements gathering, Design, Implementation, Testing, and Deployment, is completed sequentially. It is well-suited for projects with stable, well-defined requirements but lacks flexibility for changes once a phase is complete. Agile on the other hand is an iterative and customer-centric approach emphasizing flexibility and enabling quick changes. It breaks projects into smaller, manageable iterations (Sprints) where features are developed incrementally. It prioritizes interactions, working software, customer collaboration, and adaptability. However, Agile can be complex to implement and resource-intensive due to its continuous involvement of stakeholders and ongoing iteration. Despite these challenges, Agile is well-suited for projects with dynamic requirements and where rapid delivery of value is prioritized.
2. **Why is Agile suitable?:** In the dynamic online retail environment, market and customer needs evolve rapidly, therefore Agile is an appropriate methodology because of its adaptability to evolving requirements, emphasis on continuous feedback, ability to deliver value quickly, and facilitation of collaboration and transparency within the team and with stakeholders. This means we can achieve progress and deliver value to stakeholders more rapidly than with a traditional Waterfall approach.

3. **Need for Teamwork and Project Management:** For a successful e-Commerce website development project, teamwork is paramount as it brings together diverse skills and perspectives for comprehensive execution. It enables collaborative problem-solving, fostering efficient communication, and promoting an environment of enhanced creativity. These aspects are essential for navigating project complexities and achieving desired outcomes. Similarly, project management is indispensable for efficient progress and success, ensuring timeline adherence, resource optimization, risk mitigation, stakeholder engagement, quality control, and informed decision-making throughout the project lifecycle.
4. **What software we used and why?:** We utilized ClickUp extensively to streamline our project management processes. It is a comprehensive project management tool that offers a wide range of features to help teams plan, organize, and track their work effectively. From creating tasks for each aspect of the project, generating progress reports to organizing tasks into sprints, ClickUp served as a single platform for all project-related activities, eliminating the need for multiple tools. Our team was able to collaborate efficiently, track progress effectively, and stay organized throughout the e-Commerce website development project. The platform's versatile features and Agile methodology integration contributed to the successful completion of tasks and the overall project.
5. **Need for Project Charter and Team Charter:** Creating a team charter or project charter involves several key requirements that lay the groundwork for a successful project. To have a clear understanding of the project's purpose and boundaries defining the scope of the project is essential. To establish roles and responsibilities of each of the team members along with a communication plan, a risk management plan, quality standards ensures effective collaboration and keeps everyone informed. Additionally, frequency of updates, reporting mechanisms and clear resource allocation details avoid misunderstandings and ensure everyone is on the same page. Secondly, involving stakeholders in the charter development fosters buy-in and commitment to project success. Furthermore, it serves as a guiding framework for decision-making, change management, and problem-solving throughout the project.

Project Charter					
Project Title		E - commerce Website Development		Project Manager	Dhruv Patel
Project Start Date	Febraury 26, 2024	Project End Date	24th April, 2024	Project Sponsor	Phoebe Boyles
Business Need					
Sugar Sprout provide a diverse range of dessert mixes that capture the essence of global flavors, catering to a wide array of tastes and preferences. Implementing features like hampers to enhance customer engagement and providing value-added incentives for purchases. Offer high-quality, consistent products and developing a user-friendly e-Commerce platform with features such as category browsing and filtering options empower customers to find their perfect dessert easily, fostering satisfaction and encouraging repeat visits.					
Project Scope			Deliverables		
Project planning and coordination Timeline management. Ensure seamless user experience. Implement custom features, manage data integration.			1. A fully structured project report needs to be submitted (with the exact date range and where the resources provided have been utilized).		
			2. Fully customisable website with all the requirements put forth by the client		
Risks and Issues			Assumptions/ Dependencies		
Customization Complexity			1. All the product SKUs must be valid as per the stock count/inventory and the raw materials. 2. The project report submitted to the manager should be reported to the CEO. 3. The website design will be based on predefined templates and customization options provided by Shopify.		
Data Import Issues					
Timeline Delays					
Financials					
The budget deployed for the project is variable £5000 (additional £1000 could be deployed depending upon the requirement.)					
Miltestone				Target Completion Date	Actual Date
Project planning				March 3, 2024	March 6, 2024
Website Content				March 19, 2024	March 19, 2024
Shopify Setup and Theme Customisation				April 1, 2024	April 3, 2024
Product Setup and Integration				April 3, 2024	April 3, 2024
Website Customisation and User Functionality				April 3, 2024	April 4, 2024
Testing and Quality Assurance Completion				April 18, 2024	April 18, 2024
Documentation				April 24, 2024	April 25, 2024
Project Team			Approval / Review Committee		
Project Manager and Documentation specialist	Dhruv Patel		Sponsor	Phoebe Boyles	
	Rutvi Rakholia		Management Head	Dave Mistry	
Other team members	Akarshit Mahajan		Finance Manager	George Lintern	
	Moin Madhani				


Project Charter (Above)

Team Charter							
Members	Dhruv Patel	Rutvi Rakholia	Moin Madhani	Akarshit Mahajan	Phoebe Boyles	Dave Mistry	George Lintern
Roles	Project Manager	Front - End developer	Content Manager	Backend developer	Sponsor	Management Head	Finance Manager
Goals / Objectives	Ensure successful delivery and launch of the e-commerce store.	Customize a suitable theme to reflect the branding of the dessert shop.	Populate the website with products and engaging content.	Integrate necessary functionalities like payment gateways and shipping options.	Ensures that the funding of the project never lacks and there is consistent deployment of resources as per the requirement	Maintains coordination between both the parties and keeps a regular check on the progress of the project	Keeps a record of all the funds given to the party and ensures there is no disparity
Milestones	Within a timeframe of two months working on the project, the team member ensured that there is proper communication and integration with the delivery partners at Sugar Sprout.	By the end of the very first month, it was ensured on her part to get done with the look and feel of the custom shop. The focus of the second month was primarily on ensuring that every product added to the store blends well with the brand integrity.	Coordinating with the other party regarding the product images to ensure that all images have the proper background to match the brand theme.	Got the hold of payment gateways from the client (user credentials, multiple payment options) and made sure the pricing of the products are dynamically updated on the basis of user location, the weight of the package and the delivery method selected.	N/A	N/A	N/A
Expectations	Responsible for overall project coordination, task delegation, timeline management, and ensuring effective communication among team members and stakeholders. Expected to lead team meetings, resolve conflicts, and monitor progress towards milestones.	Tasked with designing and implementing the user interface of the e-Commerce website, focusing on aesthetics, usability, and responsiveness across various devices and browsers.	Responsible for creating and managing content for the website, including product descriptions, images, and other textual elements. Ensures that content is accurate, engaging, and aligns with the brand identity.	Handles the development of backend functionality, including database management, server-side logic, and integration with third-party services such as payment gateways and shipping providers.	Provides guidance, support, and resources for the project, ensuring alignment with organizational goals and objectives. Acts as a liaison between the project team and senior management, advocating for project needs and facilitating decision-making.	Oversees project management activities, including resource allocation, risk management, and stakeholder engagement. Works closely with the Project Manager to address any organizational or logistical challenges that may arise.	Manages the project budget, expenses, and financial resources. Ensures that spending is aligned with project objectives and approved budgets, and monitors financial performance throughout the project lifecycle.
Team Behavior							
We will communicate in the best way for each team member to respond promptly, especially in urgent situations (i.e., phone/text/email as agreed upon).							
Every two weeks there is going to be a meeting between both the parties							


Team Charter (Above)

Project Planning

1. Gantt Chart:

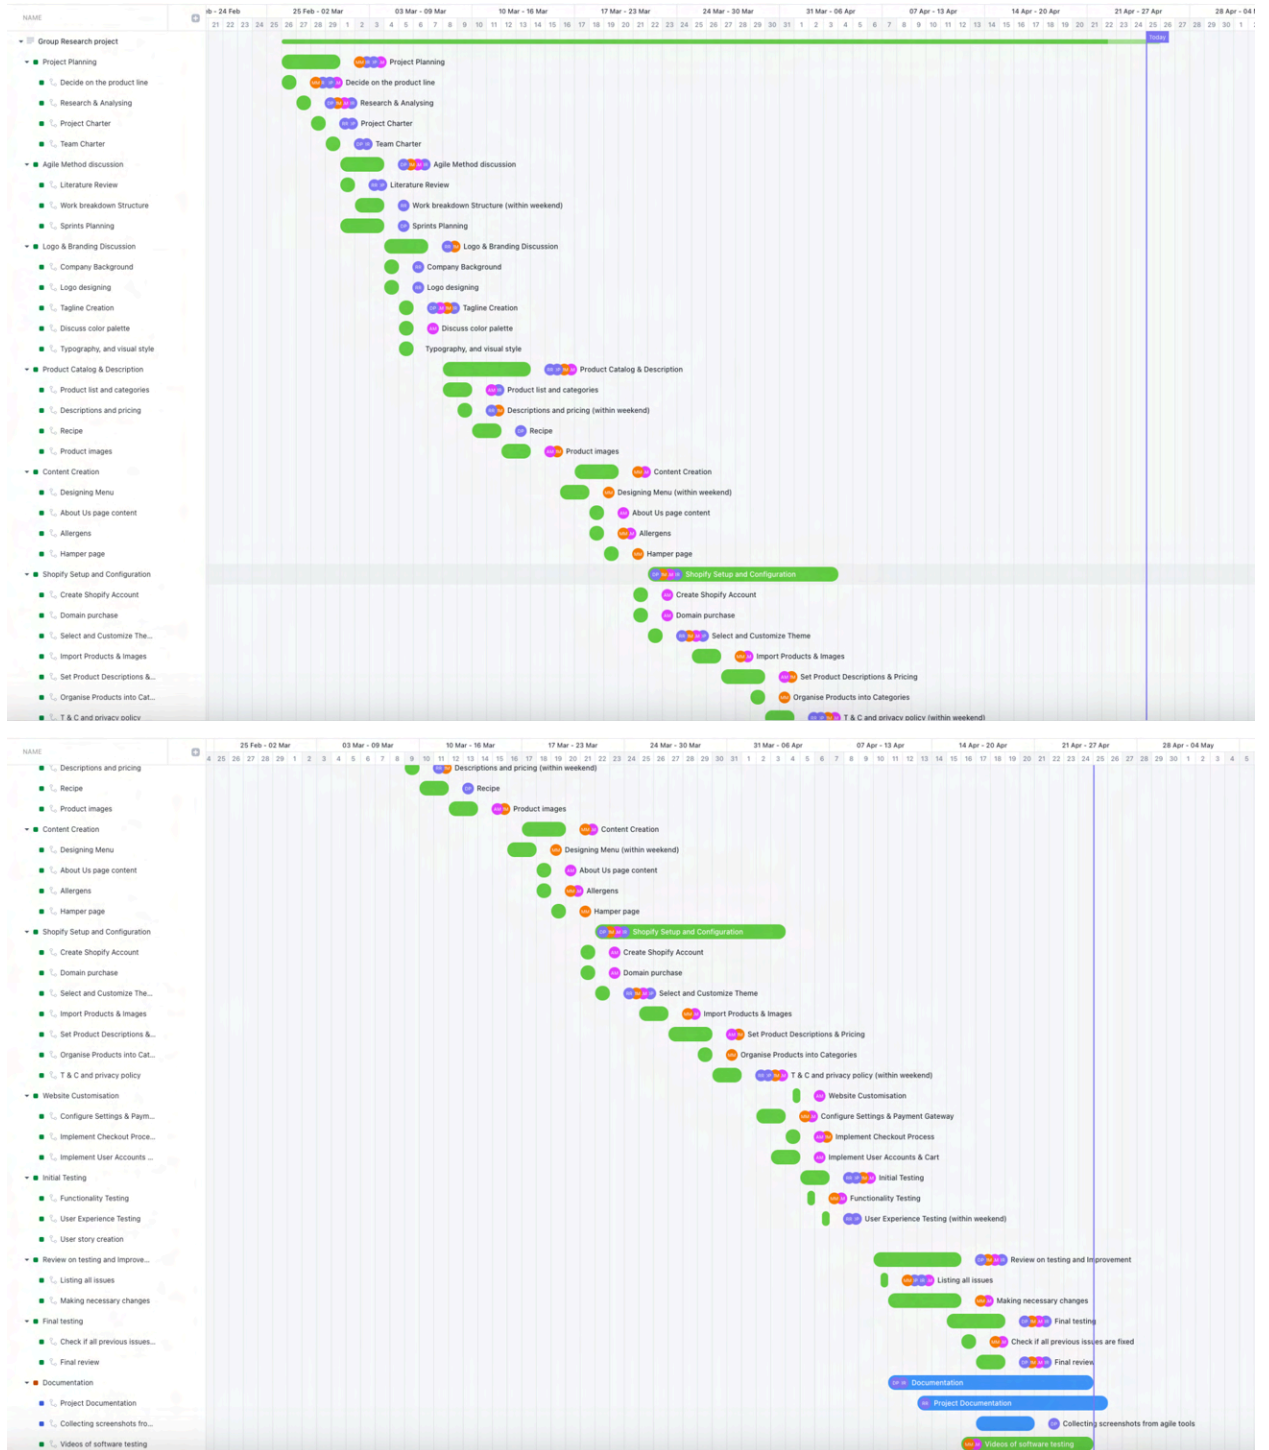

2. Work Breakdown Structure

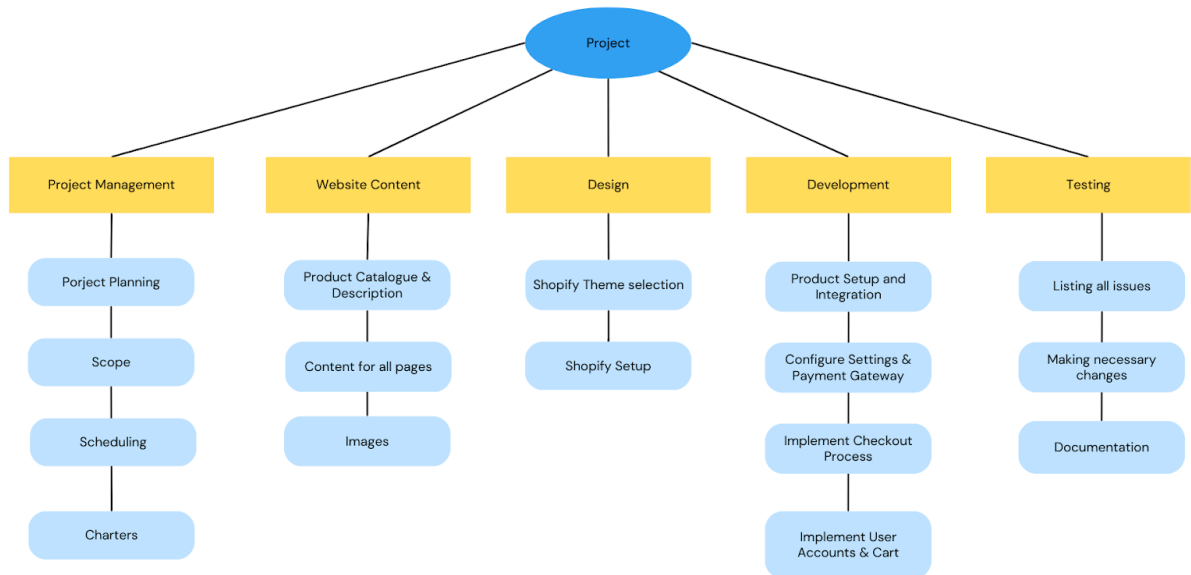

3. Sprint Backlog

Sprint 1: Sprint Goal: Main goal of this sprint is to focus on creating a charter for the project as well as the team. Along with it we have to assign a task to each member of the group and work on collecting the information regarding the SugarSprout store.

Sprint 2: Sprint Goal: Here, the goal was to acquire all the information from the store which would help us to build the e-commerce store. Information contains the product images, allergens page, designing menu, hamper page, etc. Also setting up the account on shopify and integrating with the domain was an important task in this sprint.

Sprint 3: Sprint Goal: This sprint focused on designing and uploading all the content on the store and configuring necessary steps such as payment gateway. Later to start with initial testing of the e-commerce store in order to improve and fix the bugs.

Sprint 4: Sprint Goal: This sprint focused on completing the e-commerce platform testing and finalizing the document.

Sprint 1 (Duration 26/02/2024 - 10/03/2024)

Sprint 1 14 ... + Add Task

Name	Custom Tas...	Type	Assignee	Start date	Due date	Priority
✓ Group meeting 1	—	Discussion	DP MM RR	Feb 26, 4am	Feb 26, 9:...	High
✓ Sprint planning	—	Planning	DP RR MM MM	Feb 26, 9am	Feb 27, 12...	High
✓ Approach for food industry	—	Proposal	DP	Feb 27, 9am	Feb 27, 6p...	Normal
✓ Project charter	—	Task	DP RR	Feb 28	Feb 28	High
✓ Team charter	—	Task	DP RR MM MM	Feb 29	Feb 29	Normal
✓ Literature review of the book	—	Review	DP	Mar 1	Mar 3	Normal
✓ Work breakdown structure	—	Task	RR	Mar 3	Mar 3	High
✓ Company background	—	Task	RR DP	Mar 4	Mar 5	Normal
✓ Logo designing	—	Task	MM RR	Mar 5	Mar 6	Normal
✓ Tagline creation	—	Task	MM	Mar 5	Mar 7	Low
✓ List of Products	—	Task	RR	Mar 8	Mar 9	Normal
✓ Pricing the products and writing the descri...	—	Task	RR MM	Mar 9	Mar 9	Normal
✓ Recipe of Dishes	—	Task	DP	Mar 10	Mar 10	High
✓ Scrum Meeting	—	—	DP RR MM MM	Mar 10, 7...	Mar 10, 8...	High

Sprint 2 (Duration 11/03/2024 - 24/03/2024)

Name	Assignee	Due date	Priority
✓ Group meeting	DP MM RR MM	Mar 11	Normal
✓ Recipe of dishes	DP	Mar 11	High
▼ ✓ Content Creation % 6	DP MM RR MM	Mar 19	Normal
✓ Product images	MM MM	Mar 13	Normal
✓ Group meeting (Discussion on progress)	DP MM RR MM	Mar 14	Urgent
✓ Designing Menu	MM	Mar 16	Normal
✓ About us page Content	MM	Mar 18	Normal
✓ Allergens page	MM MM	Mar 18	Low
✓ Hamper Page	MM	Mar 19	Low
▼ ✓ Shopify set-up with domain name % 3	DP MM RR MM	Mar 24	Normal
✓ Create Shopify Account	MM	Mar 21	Normal
✓ Domain purchase and linking	MM	Mar 22	Normal
✓ Select and customize theme	DP MM RR MM	Mar 24	Normal
✓ Scrum Meeting	DP MM RR MM	Mar 24	High

Sprint 3 (Duration 25/03/2024 - 07/04/2024)

Name	Assignee	Due date	Priority
✓ Group Meeting	DP, MU, RS, MU	Mar 25	High
▼ ✓ Shopify Content % 9	DP, MU, RS, MU	Apr 4	Normal
✓ Adding products	MU, MU	Mar 25	Normal
✓ Adding Images	MU, MU	Mar 26	Normal
✓ Importing product description	MU	Mar 27	Normal
✓ Set Pricing	MU	Mar 28	Normal
✓ Organise product into categories	MU	Mar 29	Normal
✓ T & C and privacy policy page	DP, MU, RS, MU	Mar 31	Normal
⚠ Configure setting and payment gateway	MU	Apr 2	Normal
⚠ Implement checkout process	MU	Apr 3	Normal
✓ Implement user account and cart	MU, MU	Apr 3	Normal
▼ ✓ Initial Testing % 3	DP, MU, RS, MU	Apr 6	Normal
✓ Functionality Testing	MU, MU	Apr 4	Normal
✓ User Experience Testing	RS, DP	Apr 5	Normal
✓ Gathering User story from users	DP, RS	Apr 6	Normal
✓ Scrum Meeting	DP, MU, RS, MU	Apr 7	High

Sprint 4 (Duration 08/04/2024 - 23/03/2024)

Name	Assignee	Due date	Priority
✓ Group meeting	DP, MU, RS, MU	Apr 8	High
▼ ✓ Review on testing and improvement % 2	DP, MU, RS, MU	Apr 15	Normal
✓ Listing all issue	DP, MU, RS, MU	Apr 10	High
✓ Making necessary changes	MU, MU	Apr 15	High
▼ ✓ Final Testing % 2	DP, MU, RS, MU	Apr 18	Normal
✓ check if all previous issues are fixed	MU, MU	Apr 16	Normal
✓ Final review	DP, MU, RS, MU	Apr 18	High
▼ ✓ Documentation % 5	DP, MU, RS, MU	2 days ago	High
✓ Project documentation	RS, DP	6 days ago	Normal
✓ Story board creation	DP, RS	5 days ago	High
✓ Collecting screenshots from agile tools	MU	5 days ago	Normal
✓ Videos of software testing	MU, MU	4 days ago	High
✓ Website documentation	MU, MU	3 days ago	High

4. **Product Backlog:** The product backlog outlines the key tasks and objectives for the development of the e-commerce platform for SugarSprout store. We started with project setup and planning, tasks by defining the project charter, team charter and assigning team roles. Then focus was on designing and configuring the store, encompassing website layout design, product and content upload, payment gateway integration, and testing of initial functionality. This ensures a systematic allowing for flexibility to incorporate additional features from the initial setup to final.

COMPLETE 11 ... + Add Task						
Name	Assignee	Due date	Priority	Comments	Status	
Project Planning		Feb 29	Normal		COMPLETE	
Agile Method discussion		Mar 3	Urgent		COMPLETE	
Product Catalog & Description		Mar 13	Urgent		COMPLETE	
Content Creation		Mar 19	Normal		COMPLETE	
Logo & Branding Discussion		Mar 6	Normal		COMPLETE	
Website Customisation		Apr 4	Normal		COMPLETE	
Shopify Setup and Configuration		Apr 3	Normal		COMPLETE	
Initial Testing		Apr 6	High		COMPLETE	
Review on testing and Improvement		Apr 15	High		COMPLETE	
Final testing		Apr 18	Normal		COMPLETE	
Documentation		Yesterday	High		COMPLETE	
+ Add Task						

5. Risk Analysis

ID	Risk Description	Likelihood Of the risk occurring	Impact if the risk occurs.	Owner (person who Will manage the risk)	Mitigating action	Contingent action	Progress on action	Status
01	Resource allocation	Medium	High	Project Sponsor	Develop a thorough resource plan by estimating workload, required skills, and project timelines. This enables early identification of the resource needs and proactive allocations	In case of resource shortages or unexpected demands, develop a contingency plan to reallocate resources from lower-priority tasks or less critical projects to ensure essential project activities are not delayed.	Maintaining the resource as much as possible.	Open
02	Integration challenge for third party payment application	Low	High	Project Manager	Conduct thorough testing, including unit tests, integration tests, and end-to-end tests, to identify and resolve any compatibility issues or bugs.	In case of integration failures or downtime with the third-party payment application, implement fallback payment options such as alternative payment gateways, manual payment processing, or offline payment methods (e.g., cash on delivery).	Gather input for continuous improvement.	Open
03	Customer Experience (delay in shipping)	Low	Low	Project Sponser	Optimise logistics and supply chain processes	Offer compensation or discounts for the inconvenience.	Keep stakeholders informed of progress and any changes.	Open

Requirement Analysis

We chose Shopify as the platform for our e-Commerce website development for its ease of use, quick setup with customizable templates, scalability to accommodate business growth, and robust built-in features essential for e-Commerce, ensuring security and reliability for our project's success. We also employed various techniques including hypothetical company background, project scope and user stories. Here's a breakdown of our requirements analysis:

1. **Hypothetical Company Background:** A Dessert shop selling signature desserts for various countries in the UK. There are 3 members in the management team including the CEO. Apart from that, there are a group of 5 people in each location 3 are chefs and 2 have a background in Hotel management. Currently they have 6 physical shops in (3) London, (1) Wales, (2) Scotland. They have set up cloud kitchens at various locations in the UK to cover places. They are currently listed on Uber eats, Just Eat, Deliveroo and have been getting many orders and are getting popular. Therefore there is a need for them to have their website so that they can give the best food experience to all of their customers. They also requested to develop a portal for chefs and delivery guys and they apply for jobs as they are looking for staff that can help them improve. They are already a well known dessert shop that sells desserts from 5 different countries and can match the expectations when people try it.
2. **Project Scope:** The scope of the project includes the design, development, and deployment of the e-commerce website using Shopify. It encompasses the integration of product catalog, shopping cart functionality, secure payment processing, and order management system serving as a digital storefront for selling products online by offering seamless shopping experience.
3. **User Stories:** Incorporating user stories ensures a user-focused approach by framing project requirements from the perspective of the end-users and, facilitating clear and concise descriptions of desired functionalities and ultimately minimizing the risk of misinterpretation or miscommunication. Agile development practices facilitate development and incremental delivery ultimately meeting requirements from the perspective of the end-users.





Evidence of Website/Online Store

The following section discusses the overall design and theme of the SugarSprout store. We discuss what all basic functionalities have been added to the store, what sort of a colour theme we are following and how the backend of the store works.

The store is hosted on Shopify and we use an in-built theme called "Sense". The basic structure of the store was provided by the theme, but we decided to start from the very scratch in order to have a good hold of the project and customize everything according to our taste. Several customizations such as relocation of all the elements, completely new home page (with an add-on plugin), and some creative decisions were made to make sure that the store looks authentic.


Layout

Logo





Header

The header is consistent throughout the website (except the checkout page). It has a menu that shows 5 different options to select from (Home, Menu, Order, Hampers, About Us, Log-in). At the same time, there is the option for the user to open their cart drawer or search throughout the store.



Footer


The footer is again consistent throughout the website (except the checkout page). It has an option for the website visitor to subscribe to the newsletter and get an exclusive discount. Simultaneously, there are the icons that show the socials of the store and a currency selector (in case the user is not from the UK). We can also see some icons of the payment methods that are currently accepted at the store.

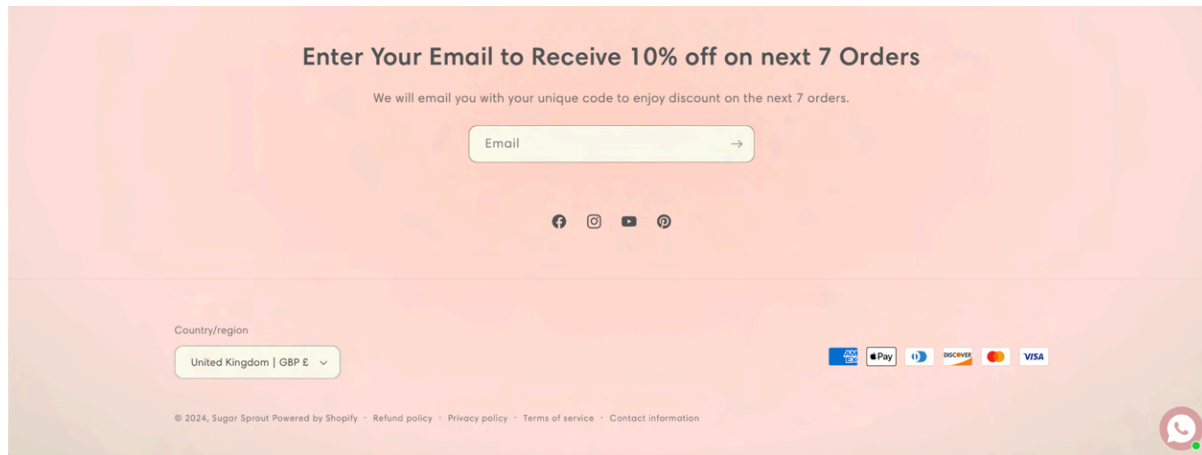

Home Page

The home page has different sections. The first section is a slideshow of different images (created inside of Figma). The second section on this page shows a different range of products available at the store, and the last section shows 5 countries from where the products are available at the store.

Link:



Order Page

This page shows a variety of sweets available at the store. The user can sort on the basis of alphabetical order, price, best selling, featured, and date added. The user can also filter by price.

Link:

<https://sugarsprout.store/collections/all>

<https://sugarsprout.store/>




Menu and Allergens Page

The page gives out the flyer-menu of the whole store (broken down into different delicacies). Along with that, it also provided a chart mentioning about the different materials the store uses to prepare the sweets so that people who are decimated by some allergies are aware beforehand ordering.

Link:

<https://sugarsprout.store/pages/how-it-work>
[S](#)




About Us Page

The page gives a background on the company SugarSprout and gives credits to each of the team members'.


Link:

<https://sugarsprout.store/pages/about-us>



Hampers Page

This page showcases different hampers (of various products grouped together) for people to purchase on festive events or as per their liking. We have four different hampers available at the store. These come in beautiful packaging and with branded tags.



Login/Register Page

This page allows the user to create their account or login if they have an existing one. They can save their add to carts, products that have been added to the wishlist or even the payment methods they previously used. The visitor also has the option to purchase without an account, but when they enter their shipping details - their account automatically


Link:

<https://sugarsprout.store/collections>

gets created on the backend.


Link:

<https://sugarsprout.store/account/login>



Cart Drawer


Instead of creating a separate page altogether, we created a simple drawer that displays when someone adds something to their cart. Results in better checkout experience and enhances the conversion rate on the website. For the mobile version, there is a separate cart page.



Product Page - #1


The product page displays a wide range of options for the user to select from. First of all, we have the image of the sweet dish itself, then on the right section - we have the button for the user to add the product to the cart or even directly click on "Buy with Apple Pay" for faster checkout. We have the option for the user to view the allergens as well.

Just below that, we have a timer that creates a sense of urgency for the user to complete the checkout before the discount code expires.



Product Page #2

The following section on the product page shows the nutritional value in a beautifully structured table and just below that, there is




Offer Pop-up

Once the user adds something to their cart, they are automatically presented with a pop-up upselling the hamper. If the user


the reviews section. This allows the buyer to add their review (along with the star rating, images, and recommendations).

decides to purchase this as well, then the average order value also goes uphill.




Checkout Page

Once someone has finalized their order, they are given an indication to purchase the product and are taken to the checkout page. This is a 1-page checkout where it asks the user to either pay via Apple Pay or they can simply use their debit or credit card to complete the payment. To build out this payment system, we linked the Shopify store to a Stripe account. The user has to add their billing and shipping address as well to confirm the order.



Discount Functionality

Each and every first time purchaser from the store is given an exclusive 20% off discount voucher. They can simply apply the coupon "FIRST20" on the checkout page to enjoy a 20% discount.



Thank You Page

Once the user has been tagged as a purchaser, they are taken to a thank you page displaying the estimated time it will take for the delivery and shows their address.

United Kingdom		
United Kingdom		
Rate name	Condition	Price
Same Day Delivery	£5.00 and up	£6.49 GBP
Standard Delivery	£0.00-£200.00	Free

Shipping and Delivery

If the purchaser is from the UK, they are presented with two different shipping options. The first one is the "Same Day Delivery" costing 6.49 GBP flat and the second shipping option is "Standard Delivery" which is free but takes 4 - 5 days for delivery. This is again presented on the checkout page after the user is done adding their billing information.

Below shows some of the add-on plugins we used to enhance the functionality of the online store. Here are some the plugins and their functionalities:

1.



Shogun Landing Page Builder

Shogun builder has been used to design the landing page and the about us page. The slideshow component has been implemented (it switches slides every 7 seconds), and is also optimized for the mobile view.

2.



Judge.me Reviews


Judge(.me) has been used to collect reviews from the user. They can only add reviews if they have placed an order on the website and have the tracking id.

3.



Chatty: Livechat & Helpdesk

Chatty has been used to provide support to the customer providing solutions on whatever stage in the buyer journey they are. They also have the option to live chat with the support at the company from 9 am to 6 pm (Mon - Fri).



(Chatty - Live Chat Support)

Website Go-through and Testing

The following YouTube channel has been specially created to prove the working of the store (for both desktop and mobile versions). The channel has several videos displaying the functioning of each & every button, the user account creation and the checkout functioning.



[\(Watch the testing videos here\)](#)

Reference

Redirecting (no date) login.microsoftonline.com. Available at:
<https://ebookcentral.proquest.com/lib/uwestlon/reader.action?docID=6327673> (Accessed: 25 April 2024).

Atlassian (no date) Get started with agile project management, Atlassian. Available at:
<https://www.atlassian.com/agile/project-management#:~:text=Agile%20project%20manageme nt%20is%20an.>

Jakes, D. (2023) What Is Waterfall Project Management?, TechnologyAdvice. Available at:
<https://technologyadvice.com/blog/information-technology/what-is-waterfall-project-managem ent/>.

Ambardekar, N. (2022) What Should I Do If I'm Allergic to Nuts?, WebMD. Available at:
<https://www.webmd.com/allergies/nut-allergy>.

Food Standards Agency (2022) Allergen Guidance for Food Businesses, Food Standards Agency. Available at:
<https://www.food.gov.uk/business-guidance/allergen-guidance-for-food-businesses>.
